

Group 11

1. Sprint Planning

Unfortunately, in the beginning we didn't know that we should screenshot the Jira, therefore we did not implement it. Despite that we wrote down what you should have seen in the screenshot:

Sprint goal:

"Create design tools for all of the modules and establish the project infrastructure"

Selected tasks:

1. Source Data Manager Design tools(Subtasks: N/V analysis, CRC cards, UML diagram)
2. Result Data Manager Design tools(Subtasks: N/V analysis, CRC cards, UML diagram)
3. Data Visualizer Design tools(Subtasks: N/V analysis, CRC cards, UML diagram)
4. Asset Manager Design tools(Subtasks: N/V analysis, CRC cards, UML diagram)
5. Optimizer Design tools(Subtasks: N/V analysis, CRC cards, UML diagram)
6. Link Jira with GitHub
7. Create the Avalonia project
8. Convert XLSX to CSV file
9. Upload CSV file to the assets folder

Every ticket was also assigned to a team of 2 people, both as assignees and as reviewers. It is also noted in the tickets comments.


Task assignment

Due to a difference in the level of experience in our team, we split up into groups of two(Maria Tsioni & Zoja Angelovicova, Pavel Seliavko & Zoe Elea Zeilmann, Dominik Bezo & Daniel Falat). Maria & Zoja took on creating the infrastructure and setup tasks along with the Source Data Manager. Pavel & Zoe took on the Asset Manager and the Optimizer and Dominik & Daniel took the Result Data Manager and the Data Visualizer.

Since Jira only allows individual assignments, each ticket was assigned to one person of the group but the team was stated in the ticket description.

Team Roles of This Sprint:

- Scrum Master → Dominik Bezo
- Meeting Coordinator → Pavel Seliavko
- Product Owner → Supervisor(Radoslaw Marek Chylak)

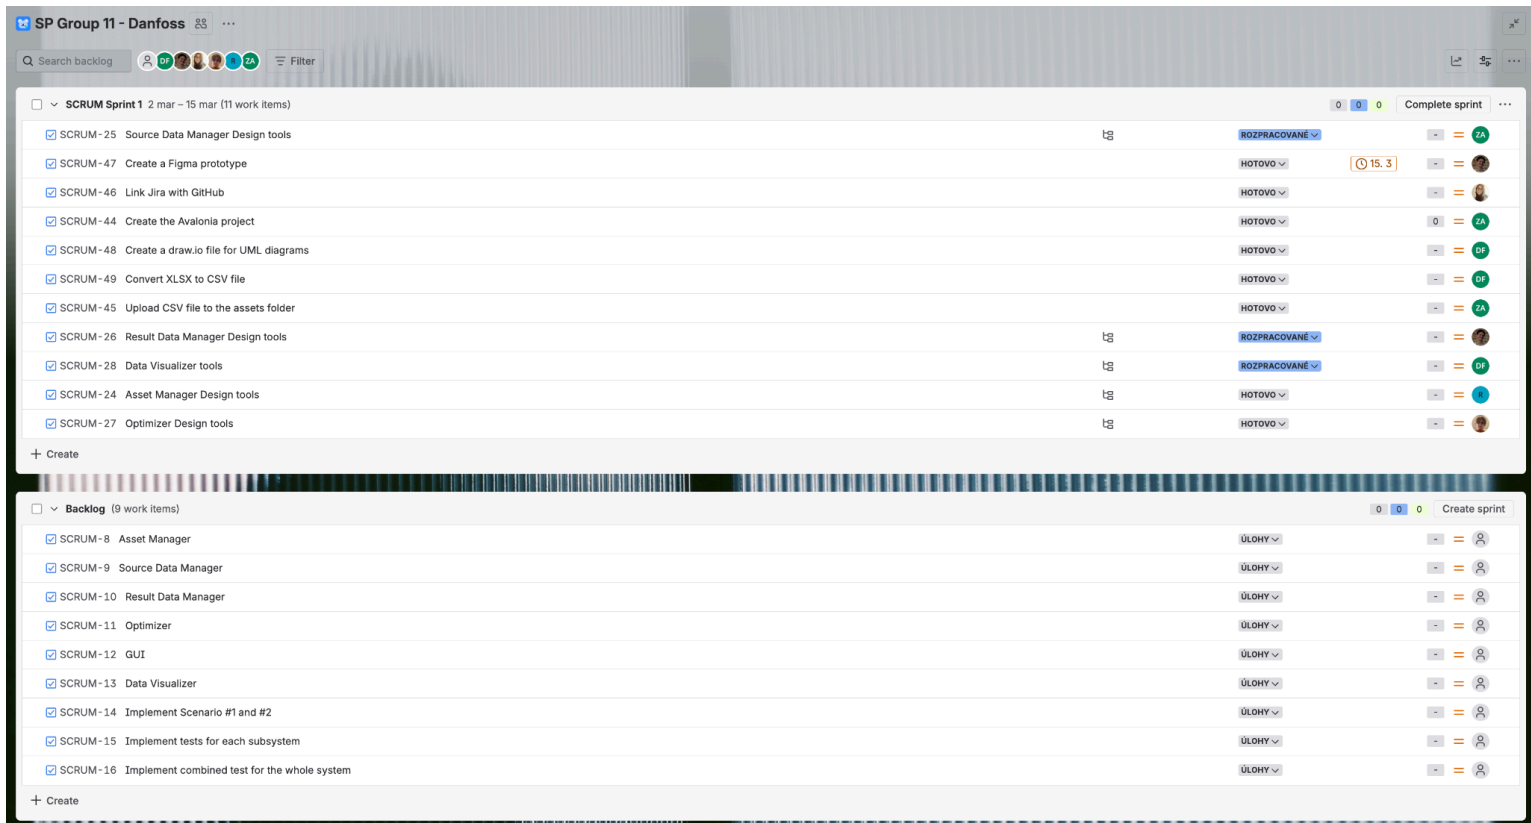

*HOTOVO - DONE, ROZPRACOVANÉ - IN PROGRESS

During the first week's Daily Standup, we realised that we have capacity to finish additional work. Initially, we wanted to start with coding the asset manager but after consulting with our supervisor we decided to create a Figma prototype along with other supporting tasks.

Some of the tasks regarding Design tools of the modules needed to be moved back to "IN PROGRESS" after being reviewed. Even though the N/V analysis subtask was moved to "DONE", the CRC cards and the UML diagrams still needed improvements, which we didn't manage to do in this sprint. These tickets were moved back to the backlog after we finished the sprint. We discussed which ones we are going to move to the 2nd sprint and agreed on the Data Visualizer. The other two remain in the backlog and we are going to implement those later.

3. Sprint Retrospective

What worked well:

- Communication between us was overall positive
- Workload was distributed evenly across the teams
- The Sprint delivered most of its goals and we even decided to take on more work than we originally planned
- Working in pairs proved to be successful

What didn't work well:

- Openness to different opinions (some team members were dismissive and resistant to ideas of other team members)
- Individuals being inactive during meetings (since most of our meetings are online it's easy to start hiding behind the screen)
- Lack of immediate feedback (we waited to bring up these two issues until the sprint retrospective and which lost us some time)
- Underestimation of the workload (in the beginning we took on too little work which resulted in unproductive days and lost time)

What will be improved:

After talking about what didn't work well, we talked about the issues and we came to some solutions:

- Firstly we talked to certain members and looked at both sides of the story. We agreed that in the future everyone should have an open mind about other people's opinions.
- For the second issue we decided that from now on we are going to turn on our cameras to create a stronger sense of presence.
- We also decided that if we disagree with actions or behaviour of a team member, we are going to approach them and talk about the problem immediately, not waiting until the Sprint Retrospective so that we can work more efficiently.
- Lastly we decided to implement an estimation of difficulty and importance of tasks for the sprints so that we can estimate more accurately the workload we should take on for each sprint. Basically, the team created their own version of story points to be implemented in the next Sprint. The system we agreed upon is to assign 1 to 5 points to both "Difficulty" and "Importance". The total number depicts the overall estimation of the ticket.

What we learned

The first Sprint taught us a lot about proper team work. We learned how to communicate constructively as a team about things we are not happy with. While the technical work went mostly well we needed to work on communicating as a group, finding solutions to certain issues that were brought up in the retrospective as are mentioned above. We already started implementing points mentioned previously in the "What will be improved" paragraph and we already could see the differences during our second Sprint Planning meeting.

4. Graphs



Regrettably, we aren't able to provide the rest of the graphs, as we didn't assign story points to our tickets from the beginning. The reason being the fact that the design process of each manager/unit was equally distributed among members and every task had the same level of importance for being completed in this Sprint. Therefore, the story points system got established for the second Sprint.
