

Group 11

- Sprint Planning

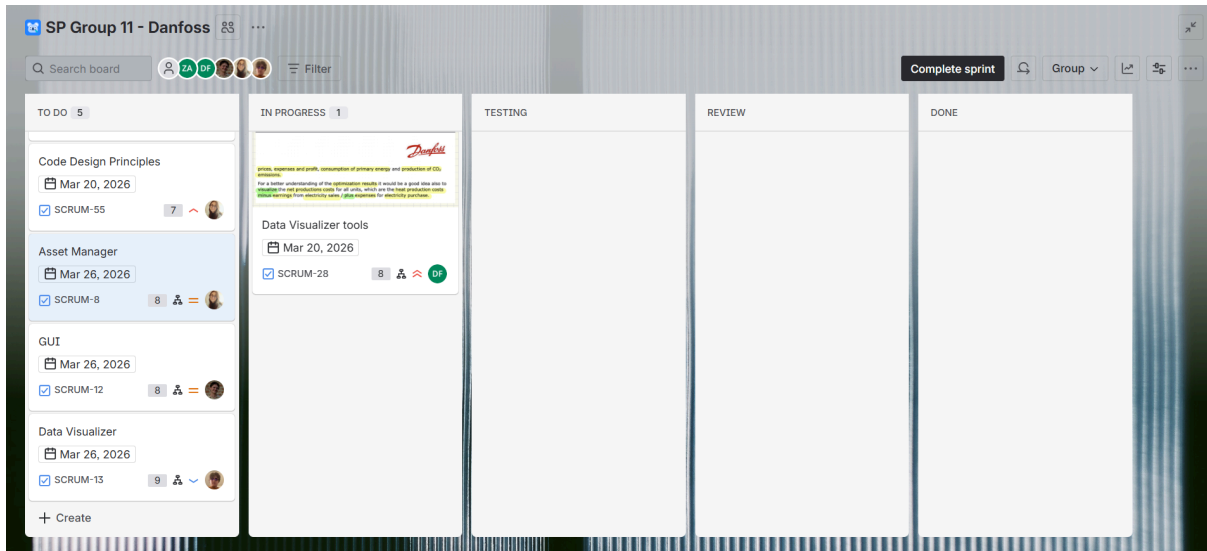


Figure 1: Screenshot of the board after starting the sprint

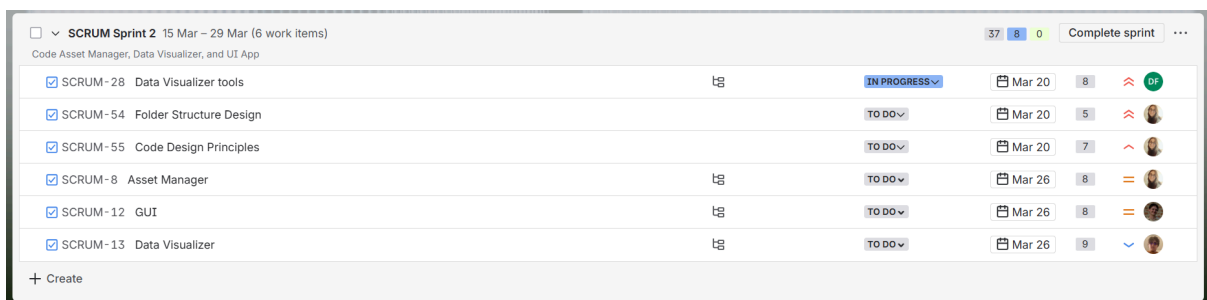


Figure 2: Screenshot of the backlog after starting the sprint

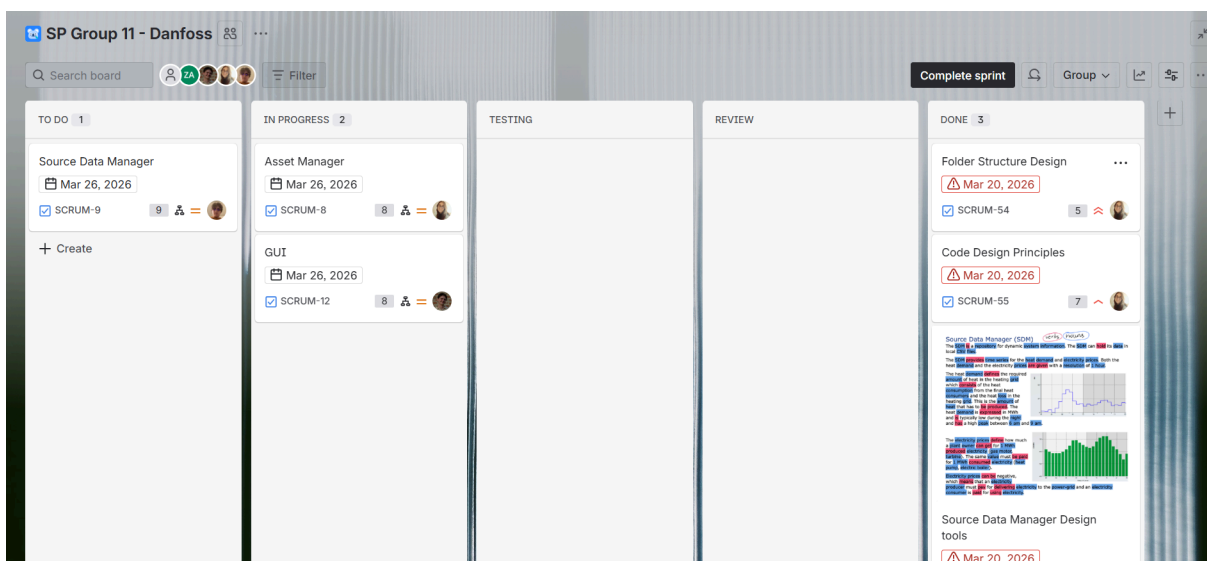


Figure 3: Screenshot of the board in the middle of the sprint, after the 1st week.

During the Sprint Planning we decided that we will focus on writing the code for the Asset Manager, Source Data Manager, Data Visualizer and begin the GUI, since we already had finished the Figma prototype on the first Sprint. Furthermore, we decided on which tickets from Sprint 1 should be improved upon in Sprint 2, and based on our plan we chose to focus on completing the design tools for the Data Visualizer.

Later, during our first meeting, we realised that we should first focus on the Source Data Manager instead of Data Visualizer. We decided to change 2 tickets regarding this. We removed the task for the Data Visualizer code and design tools improvement, and instead replaced it with the task of the Source Data Manager code and design tools improvement. Furthermore, as the sprint progressed we added smaller subtasks (e.g. improving of the UML diagram), to accommodate the initial tasks.

Lastly, in this sprint we also decided to add story points to our tickets. We used a 10 points scale, which represents the sum of difficulty and importance of a task, both on a scale of 1 – 5. As you can see in the screenshot, the Source Data Manager is worth 9 story points, 5 points for importance and 4 points for difficulty.



Figure 4: Screenshot of the assigned story points to the Source Data Manager ticket

We also decided to continue with pair programming and to keep the teams from the last sprint. In Jira we couldn't assign a task to multiple people, so as a work-around we assigned the task to one member of the group, but both team members did it. Some of the tickets were also done by the whole team. The tickets SCRUM 54 and 55, as seen in Figure 2, were implemented by the whole team on the first meeting after the sprint planning, despite the tickets having an individual assignee.

Teams this Sprint:

- Maria Tsioni & Zoja Angelovičová
- Dominik Bezo & Daniel Falat
- Pavel Seliavko & Zoe Elea Schiwy

Team Roles of This Sprint:

- Scrum Master → Pavel Seliavko
- Meeting Coordinator → Pavel Seliavko
- Product Owner → Supervisor(Radoslaw Marek Chylak)
- Documentation (eg. meeting logs) → Maria Tsioni, Zoja Angelovičová, Dominik Bezo

• Sprint Review

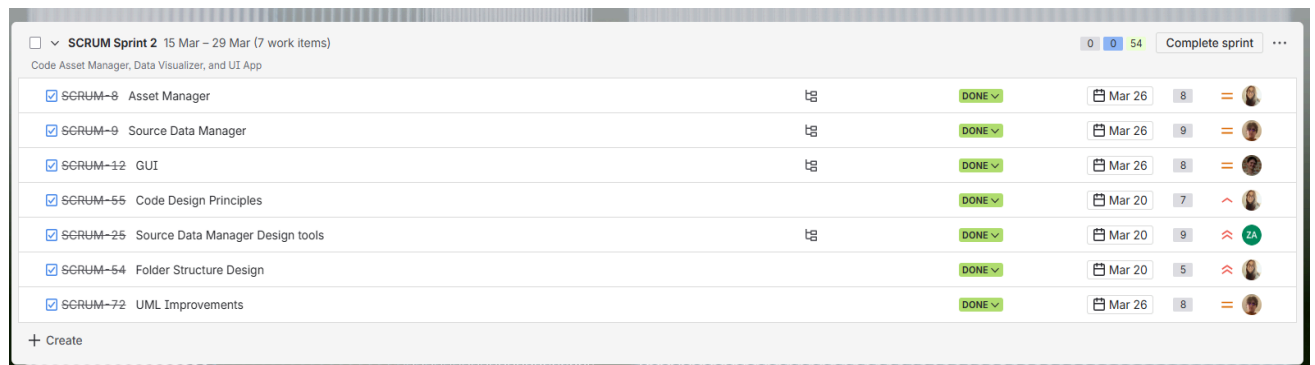


Figure 5: Screenshot of the backlog before closing the sprint

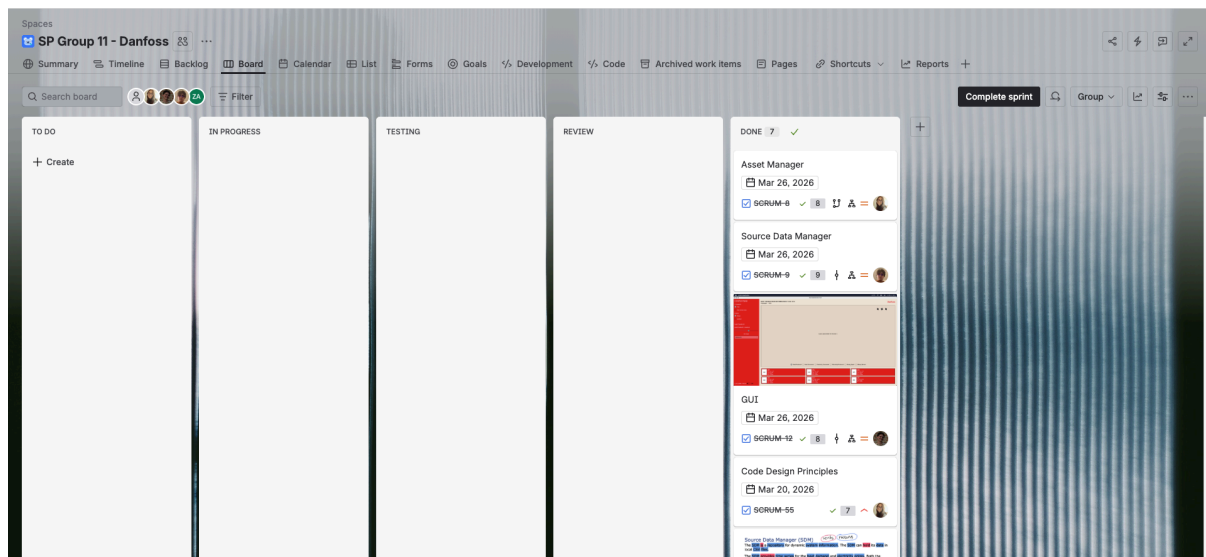


Figure 6: Screenshot of the board before closing the sprint

A significant issue identified during the sprint was the addition of new tickets midway through the process. This occurred because our initial sprint planning didn't fully account for the technical complexities involved in implementation. While we managed this by adding subtasks to existing tickets, it highlighted the need for more thorough and mindful planning in future increments. Although it is difficult to perfectly predict every challenge at the start of a task, we intend to refine our approach to sprint planning to ensure better technical foresight.

- *Sprint Retrospective*

What worked well:

- Communication worked well
- Collaboration was smooth
- Previous sprint's feedback was taken into consideration and applied

What didn't work well:

- The team did not have any negative feedback regarding pair-programming collaboration and communication. Despite that, due to schedule constraints, one group realized that it was hard finding time to work together. This resulted in the tickets taking more time than they could have taken if the team's schedules were aligned.

What will be improved:

After talking about what didn't work well, we talked about the issues and we came to some solutions:

- The primary issue identified was a scheduling conflict between certain members. However, as the team had previously agreed to rotate pair programming partners for each sprint, this problem is expected to resolve itself. In the upcoming sprint, these members will be paired with others whose availability is better aligned, preventing future delays.¹

What we learned

- We should put more thought into pairing people as the wheel of names proved to be unreliable. Previous sprint's feedback helped to solve personality issues before they become problems, as we decided to bring up our grievances as they come.

● Graphs

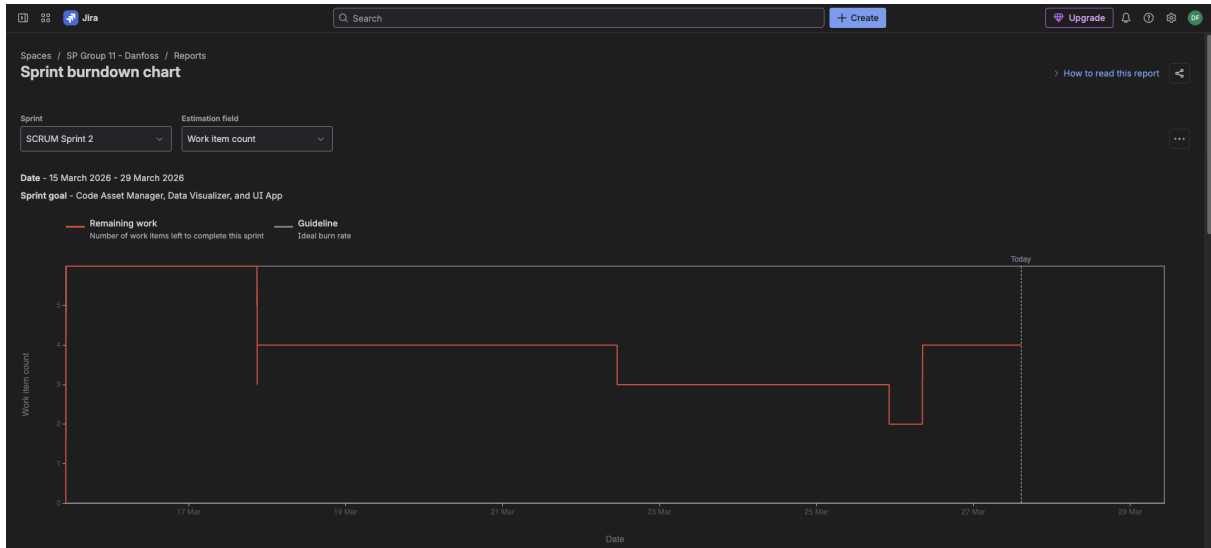


Figure 7: Sprint burndown chart - Work item count

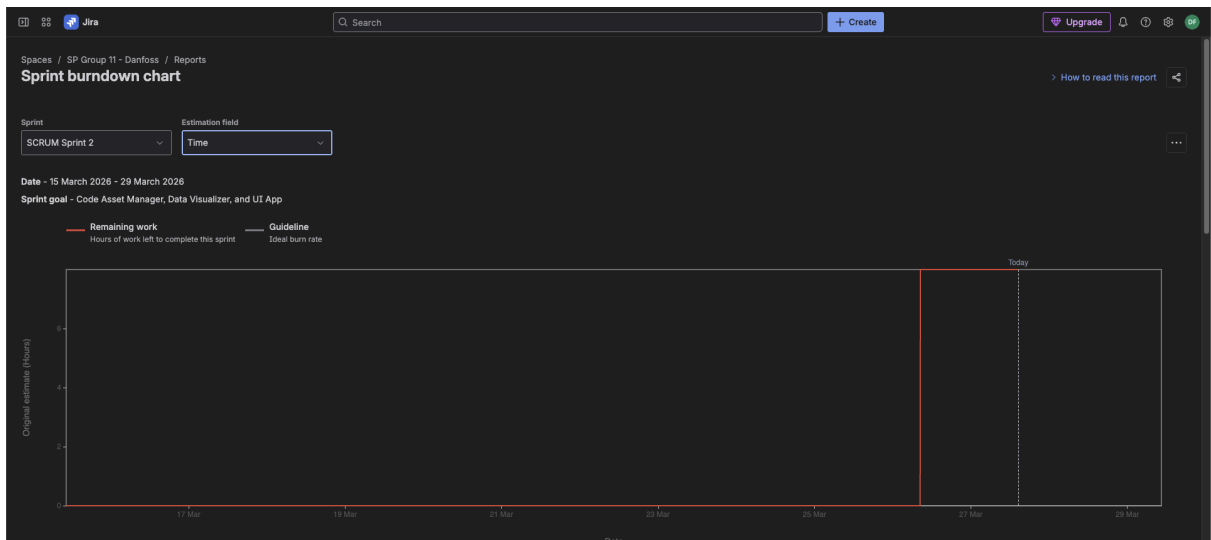


Figure 8: Sprint burndown chart - Time

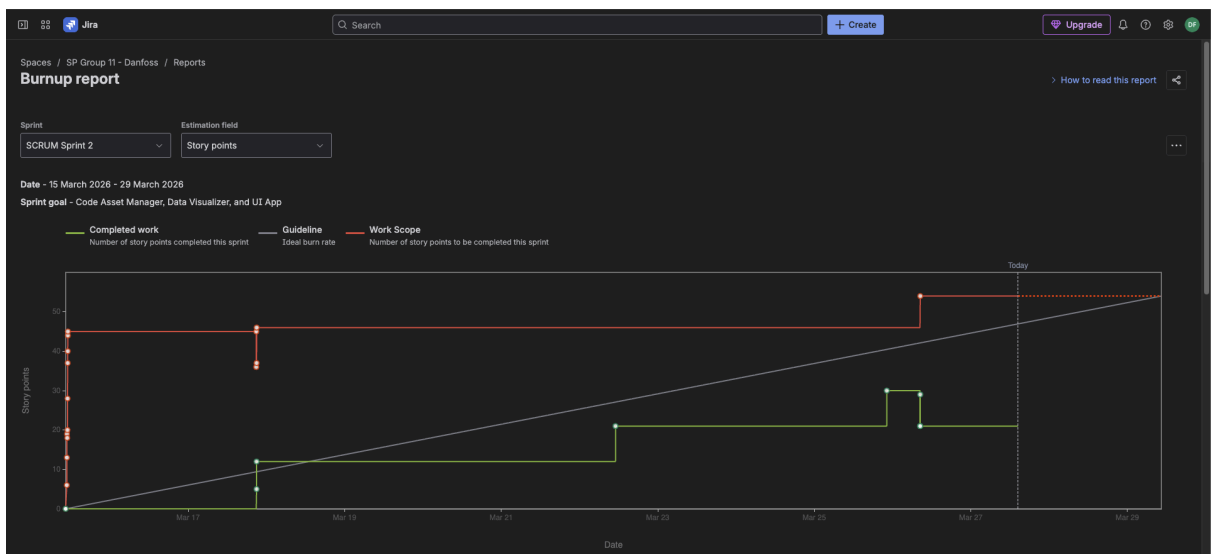


Figure 9: Sprint burndown chart - Story points

The burnout charts look incorrect, because of an error with Jira. The solution to which is unbeknownst to us. The subtasks were marked as done, yet not considered done by Jira and the same problem appeared with the tickets. Eventually, we figured it out on the last day of the sprint. Another issue was with the assigned due dates being displayed as overdue despite tasks and subtasks being in the done category. It needs further investigation in order to solve that one. The individual contribution is also skewed, because we work in pairs, but tasks and corresponding reviewers are assigned to individuals.

Add epic / SCRUM-8

Asset Manager

Key details

Priority

Medium

Original estimate

0m

Description

Create Asset Manager Class in all of its glory

importance - 5 | difficulty - 3

Subtasks

100% Done

Work	Priority	Assignee	Status
SCRUM-51 Create AssetManager class	Medium	Zoja An...	DONE
SCRUM-52 Create AssetLoader in Data folder	Medium	Zoja An...	DONE
SCRUM-53 Create Grid class in Models folder	Medium	Maria Ts...	DONE
SCRUM-60 Create git ignore	Medium	Maria Ts...	DONE
SCRUM-61 Create a branch for asset manager	Medium	Zoja An...	DONE
SCRUM-66 PULL GIT IGNORE BEFORE YOU START CODING	Medium	Unassig...	DONE
SCRUM-73 Add Images from the Asset Manager doc file	Medium	Zoja An...	DONE
SCRUM-74 Create GenericUnit in Models folder	Medium	Maria Ts...	DONE
SCRUM-76 Create JSON files for ProductionUnits & Paths	Medium	Maria Ts...	DONE
SCRUM-77 feat: Add JSON deserialization & caching pattern to AssetManager	Medium	Maria Ts...	DONE

Done

Done

Details

Time tracking

No time logged

Assignee

Maria Tsioni

Labels

None

Parent

None

Due date

Mar 26, 2026

Team

zoja & maria

Start date

None

Sprint

SCRUM Sprint 2

Story point estimate

8

Fix versions

None

Development

1 branch

Create commit

Create pull request

Reporter

Dominik Bežo

Automation

Rule executions

Created February 27, 2026 at 10:25 AM

Updated 40 minutes ago

Resolved 6 hours ago

Configure

Figure 10: Asset Manager ticket and its' subtasks

Add epic / SCRUM-9

Source Data Manager

Key details

Priority

Medium

Original estimate

0m

Description

Code a Source Data Manager

importance - 5 | difficulty - 4

Subtasks

50% Done

Work	Priority	Assignee	Status
SCRUM-63 Create a separate branch for Source Data Manager	Medium	Pavel Sel...	DONE
SCRUM-65 PULL GIT IGNORE BEFORE YOU START CODING	Medium	Pavel Sel...	DONE
SCRUM-68 Create Code for Classes	Medium	Unassig...	TO DO
SCRUM-69 Create Code for Data Retrieval	Medium	Unassig...	TO DO

Linked work items

Add linked work item

Activity

All

Comments

History

Work log

Add a comment...

Looks good!

Need help?

This is blocked...

Can you clarify...?

T

Pro tip: press **M** to comment

Done

Done

Details

Time tracking

No time logged

Assignee

Pavel Seliavko

Assign to me

Labels

None

Parent

None

Due date

Mar 26, 2026

Team

Pavel & Zoe

Start date

None

Sprint

SCRUM Sprint 2

Story point estimate

9

Fix versions

None

Open with VS Code

Development

2 branches

3 commits

2 days ago

Create pull request

Reporter

Zoja Angelovicova

Automation

Rule executions

Created February 27, 2026 at 10:25 AM

Updated 1 hour ago

Resolved 6 hours ago

Configure

Figure 11: Source Data Manager ticket and its' subtasks

Add epic

SCRUM-12

GUI

Key details

Priority

Medium

Original estimate

0m

Description

Create a layout of the GUI App

importance - 4 | difficulty - 4

Attachments

3

image-202603... 343.png

23 Mar 2026, 12:14 PM

dark.png

22 Mar 2026, 01:41 PM

light.png

22 Mar 2026, 01:41 PM

Subtasks

100% Done

Work	Priority	Assignee	Status
SCRUM-64 PULL GIT IGNORE BEFORE YOU START	Medium	DF Daniel F...	DONE
SCRUM-57 Create Subtasks	Medium	DF Daniel F...	DONE
SCRUM-62 Create a separate branch for GUI	Medium	DF Daniel F...	DONE
SCRUM-67 Create the base version of GUI	Medium	DF Daniel F...	DONE
SCRUM-58 Adjust the GUI for MVVM	Medium	DF Dominik ...	DONE
SCRUM-70 Add images of machinery into Assests folder	Medium	DF Dominik ...	DONE

Linked work items

Done

Done

Details

Time tracking

No time logged

Assignee

Dominik Bežo

Assign to me

Labels

None

Parent

None

Due date

Mar 26, 2026

Team

Daniel & Dominik

Start date

None

Sprint

SCRUM Sprint 2

Story point estimate

8

Fix versions

None

Development

1 branch

1 commit

5 days ago

Create pull request

Reporter

Pavel Seliavko

Automation

Rule executions

Created February 27, 2026 at 10:26 AM

Updated 6 hours ago

Resolved 6 hours ago

Configure

Figure 12: GUI ticket and its' subtasks
