

Group 11

● Sprint Planning

☐ ▾ SCRUM Sprint 3 6 Apr – 23 Apr (37 work items)					227	8	0	Complete sprint	...
Code the Optimizer, Result Data Manager and Data Visualizer									
☑ SCRUM-13 Data Visualizer	👤	TO DO ▾		9	⬆			ZA	
☑ SCRUM-11 Optimizer		TO DO ▾		10	=				
☑ SCRUM-28 Data Visualizer tools	👤	IN PROGRESS ▾	📅 Apr 10	8	⬆			DF	
☑ SCRUM-10 Create a branch for the Result Data Manager		TO DO ▾		5	⬆				
☑ SCRUM-26 Result Data Manager Design tools	👤	IN PROGRESS ▾		-	=				
☑ SCRUM-78 Create a layout of the report in LaTeX		TO DO ▾		-	=				
☑ SCRUM-80 Clean up of the current main branch		TO DO ▾		7	⬆				
☑ SCRUM-81 Create a copy branch named Version 1		TO DO ▾		6	⬆				
☑ SCRUM-14 Implement Scenario #1		TO DO ▾		8	⬆				
☑ SCRUM-79 Implement Scenario #2		TO DO ▾		8	▾				
☑ SCRUM-82 Merge the code		TO DO ▾		-	=			ZA	
☑ SCRUM-83 DV - Create a branch for Data Visualizer		TO DO ▾		5	⬆			ZA	
☑ SCRUM-84 Create a branch for Optimizer		TO DO ▾		5	⬆				
☑ SCRUM-85 Create Generic Unit model		TO DO ▾		7	⬆				
☑ SCRUM-86 Create Combustion Unit model		TO DO ▾		7	⬆				
☑ SCRUM-87 Create HybridUnit Class		TO DO ▾		7	⬆				
☑ SCRUM-88 Create ElectricUnit Class		TO DO ▾		7	⬆				
☑ SCRUM-89 Create Generic to Optimized Unit adapter		TO DO ▾		8	⬆				
☑ SCRUM-90 Create the ResultDataManager class in the "Services" folder		TO DO ▾		8	⬆				
☑ SCRUM-91 Create the ResultDataSaver class in "Data" folder		TO DO ▾		8	⬆				
☑ SCRUM-92 DV - Create DataVisualizer class		TO DO ▾		7	⬆			ZA	
☑ SCRUM-93 DV - Setup charting library and replace placeholder in MainWindow.axaml		TO DO ▾		8	⬆			ZA	
☑ SCRUM-94 DV - Implement SetAssets()		TO DO ▾		6	⬆			DF	
☑ SCRUM-95 DV - Implement SetSourceData()		TO DO ▾		7	⬆			DF	
☑ SCRUM-96 DV - Implement SetResultData()		TO DO ▾		7	⬆			ZA	
☑ SCRUM-97 DV - Create ChartCommand object		TO DO ▾		6	⬆			ZA	
☑ SCRUM-98 DV - Implement ShowChart(ChartCommand command)		TO DO ▾		9	⬆			DF	
☑ SCRUM-99 DV - Chart - Heat Demand		TO DO ▾		6	⬆			ZA	
☑ SCRUM-100 DV - Chart - Electricity Prices		TO DO ▾		6	⬆			DF	
☑ SCRUM-101 DV - Chart - Net Heat Production per unit		TO DO ▾		6	⬆			ZA	
☑ SCRUM-102 DV - Chart - Net Electricity Production/Consumption per unit		TO DO ▾		6	⬆			DF	
☑ SCRUM-103 DV - Chart - Expenses & Profit		TO DO ▾		6	⬆			ZA	
☑ SCRUM-104 DV - Chart - CO2 Production per unit		TO DO ▾		6	⬆			DF	
☑ SCRUM-105 DV - Chart - Primary Energy / Fuel Consumption per unit		TO DO ▾		6	⬆			ZA	
☑ SCRUM-106 DV - Chart - Net Production Costs per unit		TO DO ▾		6	⬆			DF	
☑ SCRUM-107 DV - Create DataVisualizer View with view switcher		TO DO ▾		8	⬆			DF	
☑ SCRUM-108 DV - Implement ShowHeatingGrid() and bind to image panel in UI		TO DO ▾		6	⬆			DF	
+ Create									

Figure 1: Screenshot of the backlog after starting the sprint

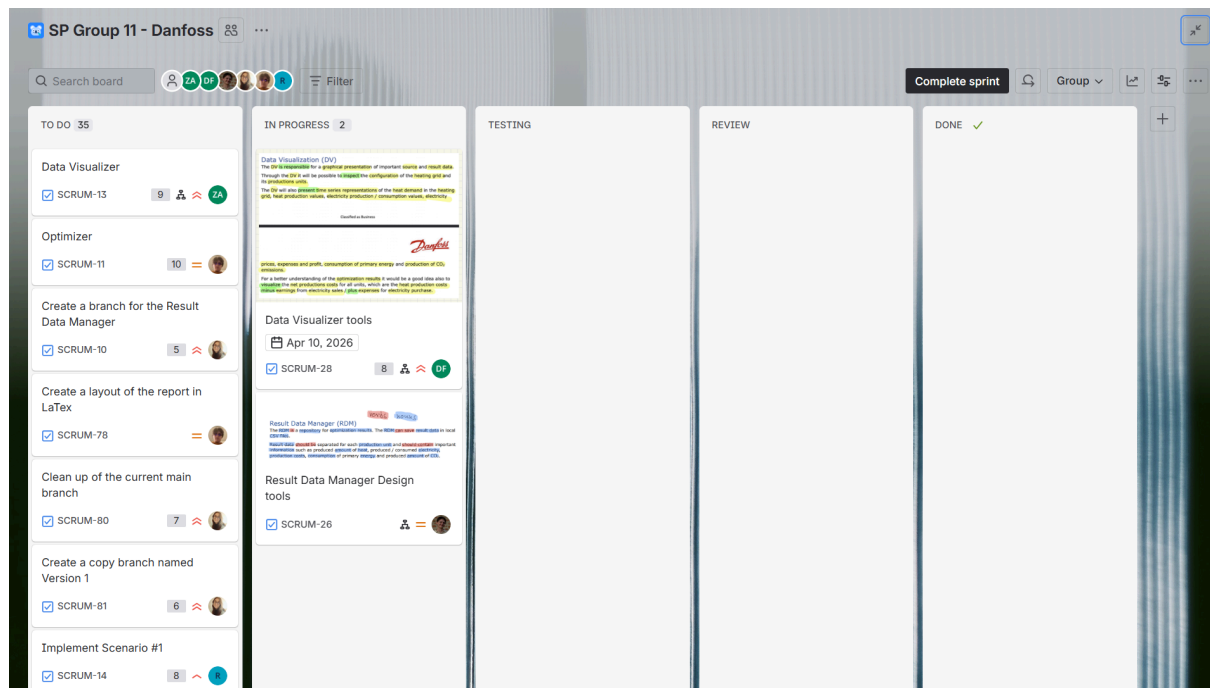


Figure 2: Screenshot of the board after starting the sprint

During the Sprint Planning we decided that we will focus on writing the code for the Optimizer, Result Data Manager and Data Visualizer, since we have already finished the other Managers during the second Sprint. In order to solve our previous Sprint's problem of adding tickets in the middle of the sprint, we decided to implement more detailed sprint planning. After dividing Managers between groups, we set a deadline and each group created their own "subtickets" for their task. Because of the problem with Jira burnout chart report from last sprint, we decided to create each subtask as a separate ticket.

During this sprint we decided to keep the story point system from the last sprint. We used a 10 points scale, which represents the sum of difficulty and importance of a task, both on a scale of 1 – 5.

We also decided to continue with pair programming. Due to scheduling issues between some of the teammates in the previous Sprint, we decided to change two teams. The teammates with more aligned schedules were paired together. In Jira we couldn't assign a task to multiple people, so as a work-around we assigned the task to one member of the group, but both team members did it. Some of the tickets were also done by the whole team. For example, the ticket "SCRUM-82 - Merge and integration of all the branches into Version-1" was done by the whole team.

Details

Assignee

 Maria Tsioni

Assign to me

Labels

None

Parent

None

Due date

None

Team

 Maria & Dominik

Figure 3: Example of how are the tickets assigned

Teams this Sprint:

- Maria Tsioni & Dominik Bežo
- Zoja Angelovičová & Daniel Falat
- Pavel Seliavko & Zoe Elea Schiwy

Team Roles of This Sprint:

- Scrum Master → Zoja Angelovičová
- Meeting Coordinator → Dominik Bežo
- Product Owner → Pavel Seliavko
- Documentation (eg. meeting logs) → Maria Tsioni, Zoja Angelovičová, Dominik Bežo

- Sprint Review

SP Group 11 - Danfoss

Search backlog

2A

BF

Filter

SCRUM Sprint 3

6 Apr – 23 Apr (38 work items)

Code the Optimizer, Result Data Manager and Data Visualizer

0

43

209

Complete sprint

☒	SCRUM-10	Create a branch for the Result Data Manager	DONE	5		
☒	SCRUM-26	Result Data Manager Design tools	DONE	9		
☒	SCRUM-00	Clean up of the current main branch	DONE	7		
☒	SCRUM-01	Create a copy branch named Version 1	DONE	6		
☒	SCRUM-04	Create a branch for Optimizer	DONE	5		
☒	SCRUM-90	Create the ResultDataManager class & Code Implementation	TESTING	8		
☒	SCRUM-05	Create Generic Unit model	DONE	7		
☒	SCRUM-06	Create Combustion Unit model	DONE	7		
☒	SCRUM-09	Create Generic to Optimized Unit adapter	DONE	8		
☒	SCRUM-14	Implement Scenario #1	DONE	8		
☒	SCRUM-07	Create HybridUnit Class	DONE	7		
☒	SCRUM-08	Create ElectricUnit Class	DONE	7		
☒	SCRUM-20	Data Visualizer tools	DONE	8	Apr 10	
☒	SCRUM-03	DV - Create a branch for Data Visualizer	DONE	5		2A
☒	SCRUM-93	DV - Setup charting library	DONE	8		2A
☒	SCRUM-94	DV - Make mock data in ResultDataManager	DONE	6		BF
☒	SCRUM-92	DV - Create DataVisualizer class	DONE	7		2A
☒	SCRUM-102	DV - Chart - Net Electricity Production/Consumption per unit	DONE	6		BF
☒	SCRUM-104	DV - Chart - CO2 Production per unit	DONE	6		BF
☒	SCRUM-106	DV - Chart - Net Production Costs per unit	DONE	6		BF
☒	SCRUM-100	DV - Implement production units dynamic binding to UI	DONE	6		BF
☒	SCRUM-99	DV - Chart - Heat Demand	DONE	6		2A
☒	SCRUM-103	DV - Chart - Expenses & Profit	DONE	6		2A
☒	SCRUM-101	DV - Chart - Net Heat Production per unit	DONE	6		2A
☒	SCRUM-105	DV - Chart - Primary Energy / Fuel Consumption per unit	DONE	6		2A
☒	SCRUM-100	DV - Chart - Electricity Prices	DONE	6		BF
☒	SCRUM-95	DV - Implement Control Panel UI Layout	DONE	7		BF
☒	SCRUM-98	DV - Connect ResultDataManager to View Model Fetching	DONE	9		BF
☒	SCRUM-107	DV - Create Dynamic Native Avalonia Chart Legend	DONE	8		BF
☒	SCRUM-96	DV - Standardize UI Colors & Theme Engine (Light/Dark Toggle)	DONE	7		2A
☒	SCRUM-97	DV - Implement Multi-metric Checkbox Grid Area	DONE	6		2A
☒	SCRUM-11	Optimizer	TESTING	10		
☒	SCRUM-91	Create the ResultDataSaver class in 'Data' folder & Implement it	TESTING	8		
☒	SCRUM-13	Data Visualizer	TESTING	9		2A
☒	SCRUM-78	Create a layout of the report in LaTex	IN PROGRESS	-		
☒	SCRUM-02	Merge and integration of all the branches into Version-1	DONE	-		2A
☒	SCRUM-79	Implement Scenario #2	DONE	8		
☒	SCRUM-109	Create the ResultDataDTO model into the 'Models' folder	IN PROGRESS	8		

+ Create

Figure 3: Screenshot of the backlog before closing the sprint

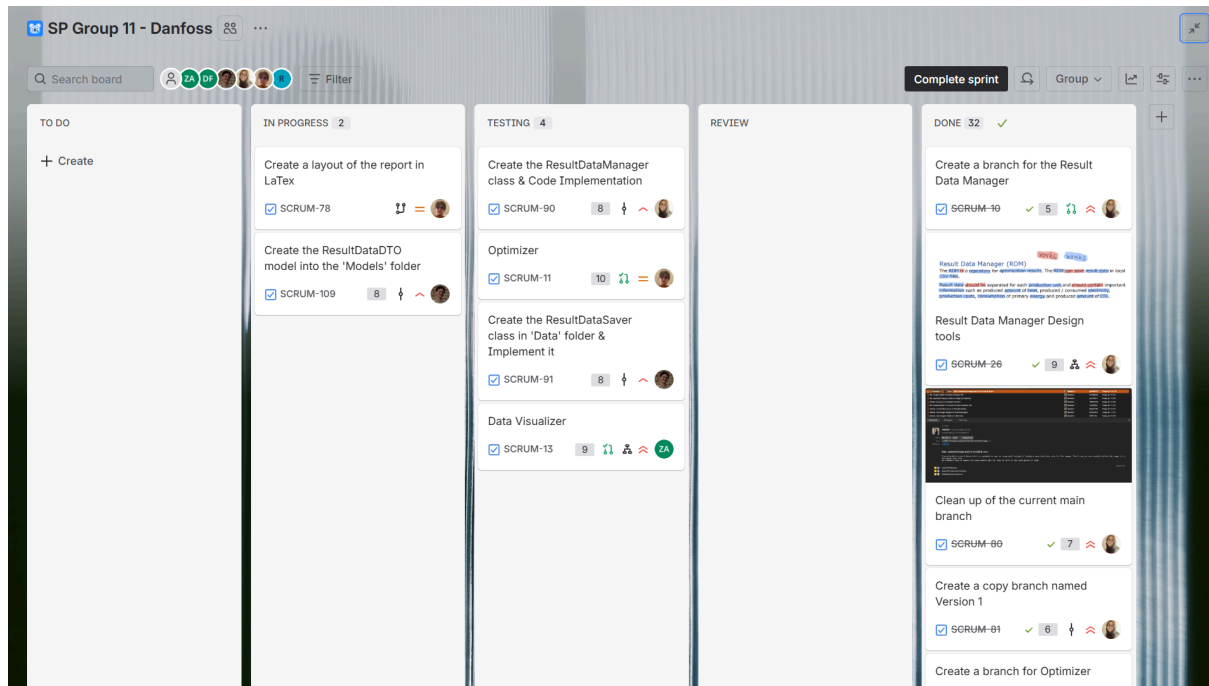


Figure 4: Screenshot of the board before closing the sprint

In the screenshots from the backlog and the board from before closing the sprint, you can see that the tickets are a little bit different then before. During implementation of the Managers we realised that some of the tasks are not relevant, so we decided to rename some of the tickets into more relevant ones.

Due to facing errors during merging of the code we decided to prolong our sprint until the 19th of april, that's why not all of our tickets are in the "DONE" category. Since the submission deadline is on the 17th of March we decided to use the latest version of the board.

● Sprint Retrospective

For this sprint retrospective we decided to do the START/STOP/CONTINUE method, conducted with "silent writing" and "round-robin sharing" methods. We also added the 'solution' column to some of the ideas.

The yellow highlighted text means we are going to implement the suggestion in the next sprint and it doesn't need any explanation or solution. On the other hand, the tasks that have the same colours in one row needed some explanation or further agreement within the team.

Start	Stop	Continue	Solutions
implement ticket ID's	having too long standup meetings, we should monitor via a timer the sprint standup meetings to not be more than they supposed to - 15min	pair programming (but also to work individually)	Next sprint keep work in groups of 3
update UML while coding, do not wait for next Sprint	test the code before the end of the sprint so it can be ready for the merge if can't test thoroughly review	documenting	
more breaks during the meeting, eg. 10 minute break every hour	not leave work for last days	ceremonies	
stricter deadlines on finishing the PI		keep the more detailed sprint planning phase	make schedule for the whole sprint, in a meeting after sprint planning
work planning before sprint planning for each individual team (eg. the weekend before the 1st week of the sprint talk on how you will work not leave it on assumption)		keep the good engagement and initiative	
clear communication		contact other people when in question	When receiving information, double check to avoid confusion, don't make assumptions
check what is already been agreed on meeting	assumptions in communication		

logs regarding code/aggreements etc. before you act			
use team calendar - No			
assign reviewers (forgot for this sprint)			
suggestion: team of 3 people for the next sprint			Teams of 3 for Unit tests for sprint 4.
update each other when things are happening do not wait for the meetings			

Table 1: START/STOP/CONTINUE table for the Sprint Retrospective

● Graphs

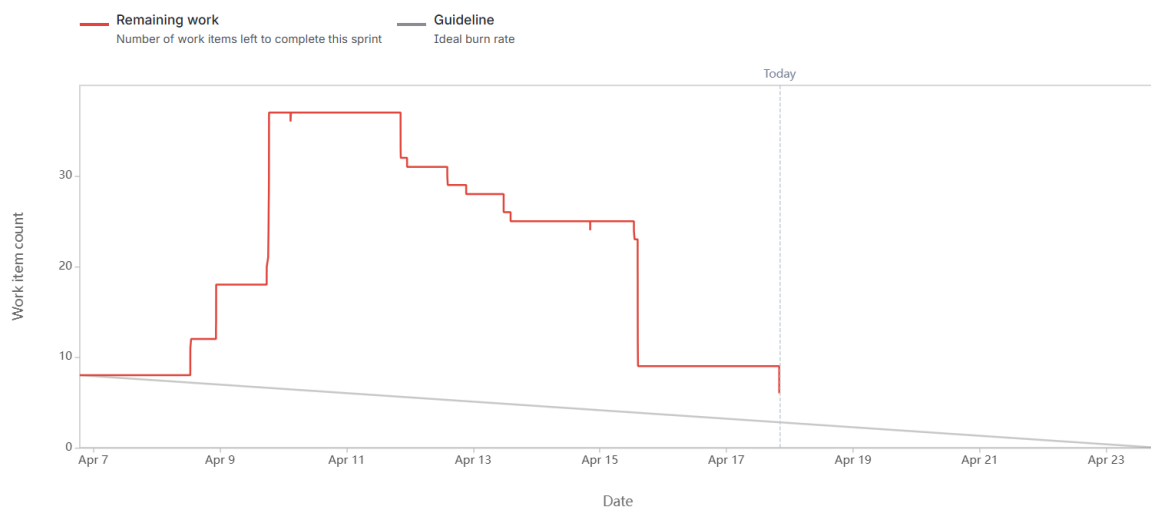


Figure 5: Sprint burndown chart – Work item count

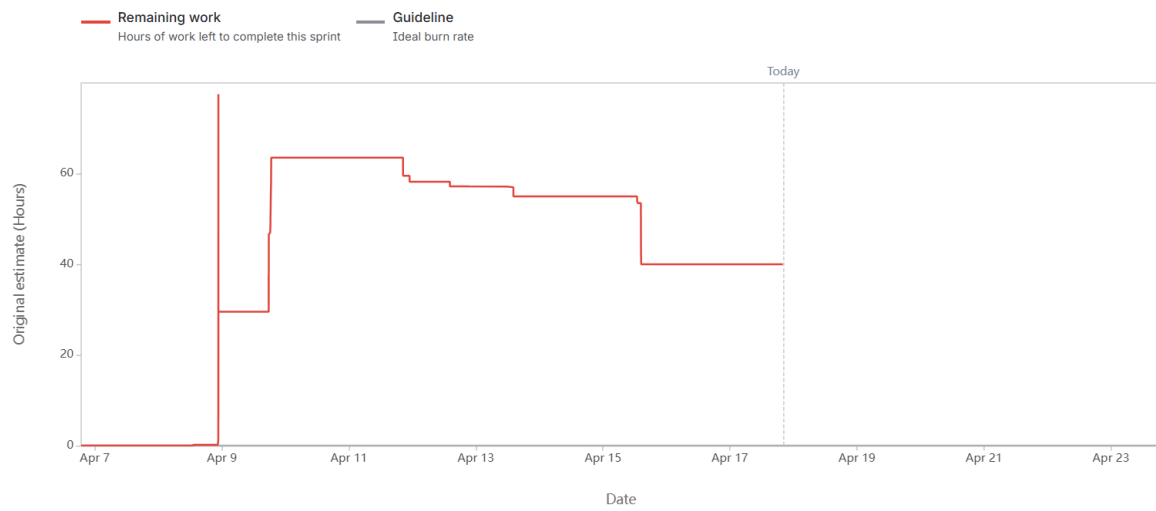


Figure 6: Sprint burndown chart - Time

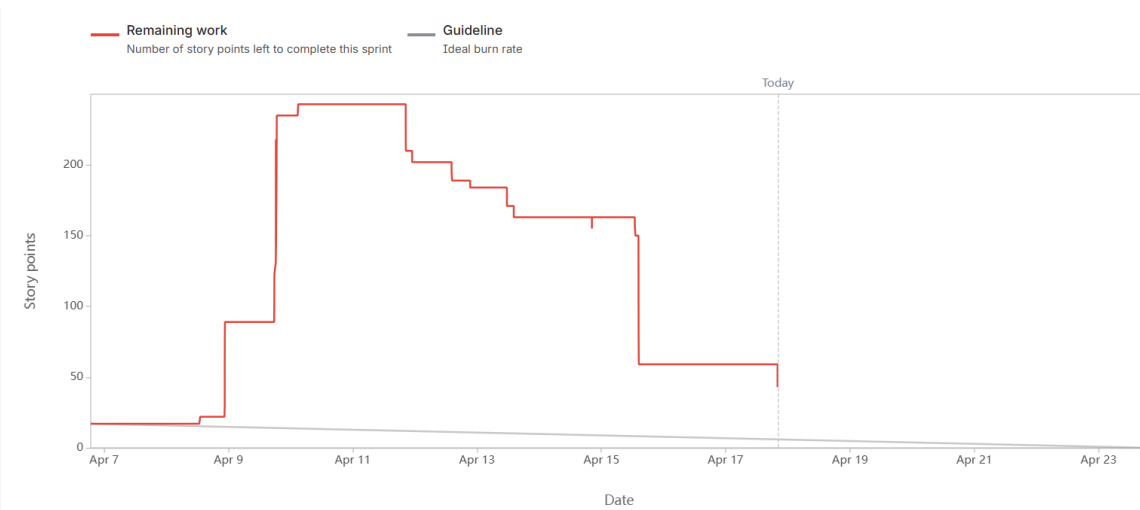


Figure 7: Sprint burndown chart - Story points
