

Group 11 – 4th Product Increment

- Sprint Planning

The screenshots unfortunately are not included, due to urgently focusing on development of the final product, we began work immediately and forgot to take screenshots of the initial backlog phase.

During the Sprint Planning we split into two teams of three. The teammates with more aligned schedules were paired together.

Teams this Sprint:

- Team Slovaks (TS): Daniel Falat, Dominik Bezo, Zoja Angelovičová
- Team International (TI): Maria Tsioni, Pavel Seliavko, Zoe Elea Schiwy

Team Roles of This Sprint:

- Scrum Master: Daniel Falat
- Meeting Coordinator: Dominik Bezo
- Product Owner: Pavel Seliavko
- Documentation (eg. meeting logs): Maria Tsioni, Zoja Angelovičová, Dominik Bežo

Things that were to be done in this sprint:

- Decide report structure – Chapters will be split amongst the group members later
- Implement scenario switching (TI)
- Refactoring of the optimizer (TI)
- Remove redundancy in the TimeSeries (TI)
- Implement maintenance selection (TS)
- Update headers for the RDM (TS)
- Update the UML to the liking of the feedback received (TS)
- Unit, Functional & Integration Tests for: AM, SDM, RDM, OPT, DV, GUI

Both of the teams made the tickets for their tasks. We decided to include the story point system from the last sprints. We used a 10 points scale, which represents the sum of difficulty and importance of a task, both on a scale of 1 – 5. We also implemented estimation of time & time actually spent on the task this sprint, assigned the groups/teams for the tickets. Each team set deadlines for individual tasks inside of their teams. When the teams complete their tasks, the tasks then will be moved to the

Review tab, to be reviewed by the other team. The review took place on Thursday 30th of April, after meeting with lecturer Amir Ghomashi.

[Back](#) [Add epic](#) / [SCRUM-122](#) [^](#) [v](#)

Implement maintenance selection in OPT

Details

Time tracking

1d logged1d remaining

Assignee

DF

Daniel Falat

Labels

None

Parent

None

Due date

26 Apr 2026

Team

👥

Daniel, Dominik, Zoja

Start date

None

Sprint

None

+1

Story point estimate

9

Fix versions

None

Development

[Open with VS Code](#)

1 branch

2 commits

[Create pull request](#)

5 days ago

Reporter

DF

Daniel Falat

Figure 1: Example of how the tickets were assigned and maintained

● Sprint Review

SP Group 11 - Danfoss

Search backlog | Filter

SCRUM Sprint 4 22 Apr - 3 May (35 work items) | 48 0 175 | Complete sprint

Item	Status	Due Date	Estimate	Assignee
SCRUM-110 Optimization Scenario Switching	DONE	Apr 24	8	[Avatar]
SCRUM-111 Optimizer check optimization correctness	DONE	Apr 23	6	[Avatar]
SCRUM-119 Create Scenario Request DTO for AM	DONE	Apr 24	6	[Avatar]
SCRUM-120 Relay Scenario Change from DV to AM	DONE	Apr 24	7	[Avatar]
SCRUM-132 Report Writing - Dominik - [parts]	TO DO	May 3	8	[Avatar]
SCRUM-133 Report Writing - Daniel - [parts]	TO DO	May 3	8	[Avatar]
SCRUM-134 Report Writing - Zoja - [parts]	TO DO	May 3	8	[Avatar]
SCRUM-136 Create project with tests	DONE	Apr 26	5	[Avatar]
SCRUM-113 RDM - Integration Test - GetResultData() - returns not empty list	DONE	Apr 28	7	[Avatar]
SCRUM-114 Create Integration Tests for RDM	DONE	Apr 29	7	[Avatar]
SCRUM-115 Create Unit Tests for OPT	DONE	Apr 29	7	[Avatar]
SCRUM-116 Create Integration Tests for OPT	DONE	Apr 29	7	[Avatar]
SCRUM-117 MVVM Unit Tests (positive & negative cases)	DONE	Apr 29	7	[Avatar]
SCRUM-118 MVVM Functional Tests (positive & negative cases)	DONE	Apr 29	7	[Avatar]
SCRUM-121 Merge MVVM Tests branch into General Tests branch	DONE	Apr 29	5	[Avatar]
SCRUM-135 OPT - Integration Test - GetResultData() - returns List<IOptimizedUnit> in both scenarios	DONE	Apr 28	7	[Avatar]
SCRUM-136 OPT - Integration Test - GetResultData() - returns correct sets of units in both scenarios	DONE	Apr 28	7	[Avatar]
SCRUM-137 Create branch for implementing the maintenance	DONE		1	[Avatar]
SCRUM-125 Update the UML diagram	DONE	Apr 26	4	[Avatar]
SCRUM-139 Merge TI's code into Version-1	DONE	Apr 29	6	[Avatar]
SCRUM-140 Merge TS's code into Version-1	DONE	Apr 29	6	[Avatar]
SCRUM-141 Validate merged code of both teams	DONE	Apr 29	7	[Avatar]
SCRUM-129 Functional Test - AM	DONE	Apr 29	6	[Avatar]
SCRUM-126 Integration Test - AM	DONE	Apr 29	6	[Avatar]
SCRUM-122 Implement maintenance selection in OPT	DONE	Apr 26	9	[Avatar]
SCRUM-123 Bind maintenance selection from UI	DONE	Apr 26	7	[Avatar]
SCRUM-124 Update headers for the RDM	DONE	Apr 26	2	[Avatar]
SCRUM-127 Integration test - SDM	DONE	Apr 29	6	[Avatar]
SCRUM-130 Functional Test - SDM	DONE	Apr 29	6	[Avatar]
SCRUM-128 Unit Test - GUI	DONE	Apr 29	6	[Avatar]
SCRUM-131 Functional Test - GUI	DONE	Apr 29	6	[Avatar]
SCRUM-112 TimeSeries<T> remove redundancy	DONE	Apr 29	4	[Avatar]
SCRUM-142 Report Writing - Maria - [parts]	TO DO	May 3	8	[Avatar]
SCRUM-143 Report Writing - Pavel - [parts]	TO DO	May 3	8	[Avatar]
SCRUM-144 Report Writing - Zoe - [parts]	TO DO	May 3	8	[Avatar]

Figure 2: Screenshot of the backlog before closing the sprint

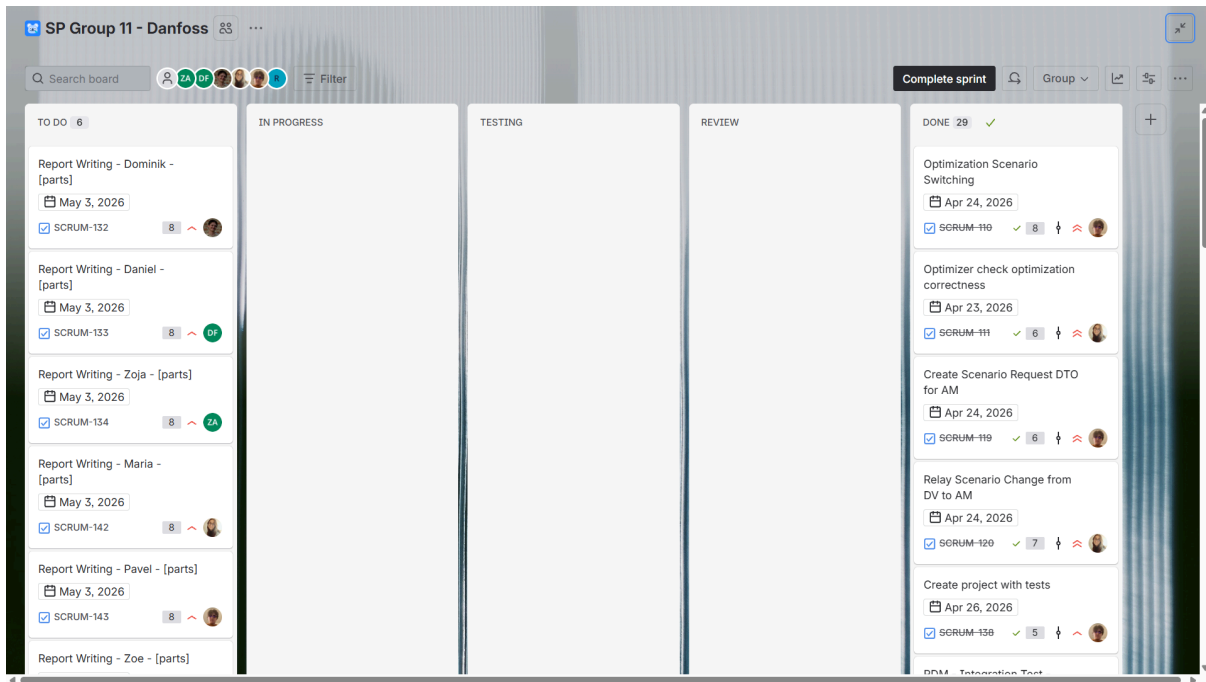


Figure 3: Screenshot of the board before closing the sprint

The sprint finished on Friday 1st of May. Due to a lot of work with testing and fixing Optimizer/Maintenance problems we did not manage to find enough time to complete Report tickets, therefore they were moved back to backlog and next sprint we will focus solely on the report writing in order to catch up with this sprint. Additionally, at the end of the sprint we realized that the two teams created the same solution to different tickets (TI Jira tickets: SCRUM 117 & 118 | TS Jira tickets: SCRUM 128 & 131), which resulted in duplicate code solutions. We decided that we will keep the redundant duplicate code just for documentation reasons of the coding process. Codewise we meet all the requirements this time, therefore we will finish the report and eventually make minor adjustments and some refactoring in the source code in the next sprint.

During the sprint review meeting we concluded that we successfully completed the initial goal of this sprint. We finished the minimum viable product, we tested it and verified that the product is working. Initially we had planned to finish a part of the report in this sprint as well, despite that the technical product increment is complete. In conclusion, the sprint was successful.

● Sprint Retrospective

As the work item count burnup report shows the teams efficiently managed to conclude the tickets on time and within the original deadlines. That indicates that the teams communicated well and worked coherently. We, ourselves, in the Sprint Retrospective confirmed that, indeed, we worked successfully and in union, with good communication inside the corresponding teams. Despite that, we had to face a

productivity loss due to misunderstanding during the Sprint Planning, which led to assumptions resulting in the duplicate code solution on two different Jira tickets. Additionally, we made an overestimation during Sprint Planning, where we added more tickets than we could solve in this Sprint. For that reason, we moved them back to the Product Backlog and we will continue working on them in the next Sprint after proper discussion and more thorough planning.

Finally, we reckoned that a more detailed Sprint Retrospective (e.g. START/STOP/CONTINUE method) would be redundant in this Sprint, since all of the team members were satisfied with the collaboration within the team.

● Graphs

Date - April 22nd, 2026 - May 3rd, 2026

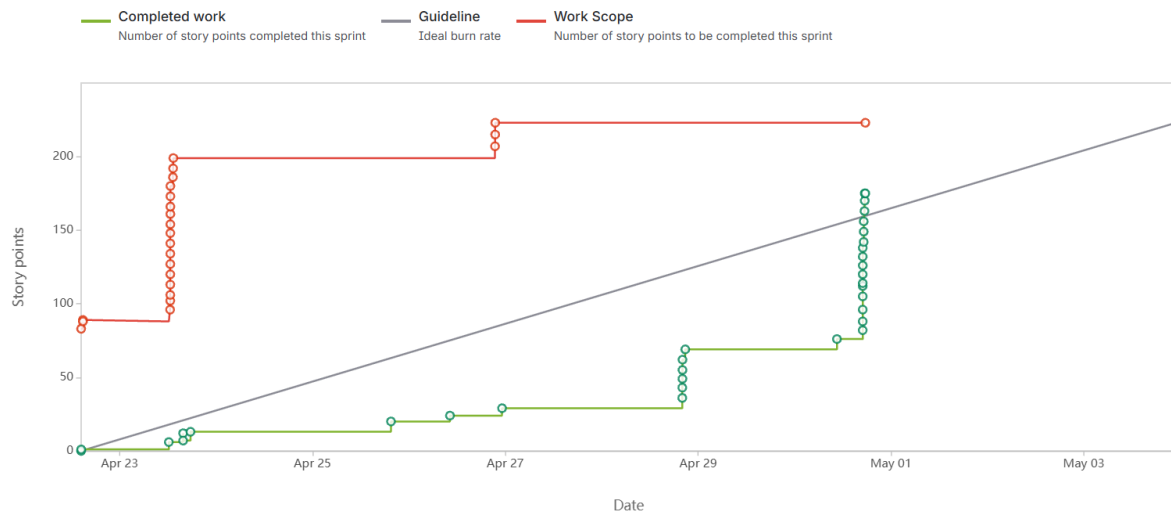


Figure 4: Sprint burnup - Story points

All work

Apps ▾ Share ▾

Basic JQL Space ▾ Assignee ▾ Type ▾ Status ▾ Key × More filters ▾ Clear filters Save filter

☐ Work	Assignee	Priority	Status	Created	Due date	
☐ SERUM-141 Validate merged code of both teams	Unassigned	Medium	DONE ▾	Apr 23, 2026, 1:20 PM	Apr 29, 2026	...
☐ SERUM-140 Merge TS's code into Version-1	Unassigned	Medium	DONE ▾	Apr 23, 2026, 1:18 PM	Apr 29, 2026	...
☐ SERUM-139 Merge TI's code into Version-1	Unassigned	Medium	DONE ▾	Apr 23, 2026, 1:15 PM	Apr 29, 2026	...
☐ SERUM-138 Create project with tests	Pavel Seliavko	High	DONE ▾	Apr 22, 2026, 2:51 PM	Apr 26, 2026	...
☐ SERUM-137 Create branch for implementing the maintena...	Dominik Bežo	Medium	DONE ▾	Apr 22, 2026, 2:05 PM	None	...
☐ SERUM-136 OPT - Integration Test - GetResultData() - ret...	Maria Tsioni	Medium	DONE ▾	Apr 21, 2026, 10:08 PM	Apr 28, 2026	...
☐ SERUM-135 OPT - Integration Test - GetResultData() - ret...	Pavel Seliavko	Medium	DONE ▾	Apr 21, 2026, 10:08 PM	Apr 28, 2026	...
☐ SERUM-131 Functional Test - GUI	Zoja Angelovicova	Medium	DONE ▾	Apr 21, 2026, 9:48 PM	Apr 29, 2026	...
☐ SERUM-130 Functional Test - SDM	Daniel Falat	Medium	DONE ▾	Apr 21, 2026, 9:48 PM	Apr 29, 2026	...
☐ SERUM-129 Functional Test - AM	Dominik Bežo	Medium	DONE ▾	Apr 21, 2026, 9:48 PM	Apr 29, 2026	...
☐ SERUM-128 Unit Test - GUI	Zoja Angelovicova	Medium	DONE ▾	Apr 21, 2026, 9:47 PM	Apr 29, 2026	...
☐ SERUM-127 Integration test - SDM	Daniel Falat	Medium	DONE ▾	Apr 21, 2026, 9:47 PM	Apr 29, 2026	...
☐ SERUM-126 Integration Test - AM	Dominik Bežo	Medium	DONE ▾	Apr 21, 2026, 9:47 PM	Apr 29, 2026	...
☐ SERUM-125 Update the UML diagram	Zoja Angelovicova	Medium	DONE ▾	Apr 21, 2026, 9:46 PM	Apr 26, 2026	...

29 of 29

All work

Apps

Share

Basic

JQL

Q Search work

Space

Assignee

Type

Status

Key

More filters

Clear filters

Save filter

☐ Work	Assignee	Priority	Status	Created	Due date	
☒ SCRUM-124 Update headers for the RDM	Dominik Bežo	Low	DONE	Apr 21, 2026, 9:45 PM	Apr 26, 2026	...
☒ SCRUM-123 Bind maintenance selection from UI	Daniel Falat	Highest	DONE	Apr 21, 2026, 9:45 PM	Apr 26, 2026	...
☒ SCRUM-122 Implement maintenance selection in OPT	Daniel Falat	Highest	DONE	Apr 21, 2026, 9:45 PM	Apr 26, 2026	...
☒ SCRUM-121 Merge MVVM Tests branch into General Tests...	Ria	Medium	DONE	Apr 21, 2026, 9:36 PM	Apr 29, 2026	...
☒ SCRUM-120 Relay Scenario Change from DV to AM	Maria Tsioni	Highest	DONE	Apr 21, 2026, 9:21 PM	Apr 24, 2026	...
☒ SCRUM-119 Create Scenario Request DTO for AM	Pavel Seliavko	Highest	DONE	Apr 21, 2026, 9:19 PM	Apr 24, 2026	...
☒ SCRUM-118 MVVM Functional Tests (positive & negative c...	Ria	Medium	DONE	Apr 21, 2026, 9:11 PM	Apr 29, 2026	...
☒ SCRUM-117 MVVM Unit Tests (positive & negative cases)	Maria Tsioni	Medium	DONE	Apr 21, 2026, 9:11 PM	Apr 29, 2026	...
☒ SCRUM-116 Create Integration Tests for OPT	Pavel Seliavko	Medium	DONE	Apr 21, 2026, 9:11 PM	Apr 29, 2026	...
☒ SCRUM-115 Create Unit Tests for OPT	Pavel Seliavko	Medium	DONE	Apr 21, 2026, 9:11 PM	Apr 29, 2026	...
☒ SCRUM-114 Create Integration Tests for RDM	Maria Tsioni	Medium	DONE	Apr 21, 2026, 9:11 PM	Apr 29, 2026	...
☒ SCRUM-113 RDM - Integration Test - GetResultData() - ret...	Maria Tsioni	Medium	DONE	Apr 21, 2026, 9:11 PM	Apr 28, 2026	...
☒ SCRUM-112 TimeSeries<T> remove redundancy	Ria	Low	DONE	Apr 21, 2026, 9:10 PM	Apr 29, 2026	...
☒ SCRUM-111 Optimizer check optimization correctness	Maria Tsioni	Highest	DONE	Apr 21, 2026, 9:10 PM	Apr 23, 2026	...

29 of 29

☒ SCRUM-110 Optimization Scenario Switching	Pavel Seliavko	Highest	DONE	Apr 21, 2026, 9:09 PM	Apr 24, 2026	...
---	----------------	---------	------	-----------------------	--------------	-----

29 of 29

Figure 5: Completed work items

All work

Apps

Share

Basic

JQL

Q Search work

Space

Assignee

Type

Status

Key

More filters

Clear filters

Save filter

☐ Work	Assignee	Priority	Status	Created	Due date	
☒ SCRUM-144 Report Writing - Zoe - [parts]	Ria	High	TO DO	Apr 26, 2026, 9:25 PM	May 03, 2026	...
☒ SCRUM-143 Report Writing - Pavel - [parts]	Pavel Seliavko	High	TO DO	Apr 26, 2026, 9:25 PM	May 03, 2026	...
☒ SCRUM-142 Report Writing - Maria - [parts]	Maria Tsioni	High	TO DO	Apr 26, 2026, 9:25 PM	May 03, 2026	...
☒ SCRUM-134 Report Writing - Zoja - [parts]	Zoja Angelovicova	High	TO DO	Apr 21, 2026, 9:56 PM	May 03, 2026	...
☒ SCRUM-133 Report Writing - Daniel - [parts]	Daniel Falat	High	TO DO	Apr 21, 2026, 9:56 PM	May 03, 2026	...
☒ SCRUM-132 Report Writing - Dominik - [parts]	Dominik Bežo	High	TO DO	Apr 21, 2026, 9:56 PM	May 03, 2026	...

6 of 6

Figure 6: Incompleted work items

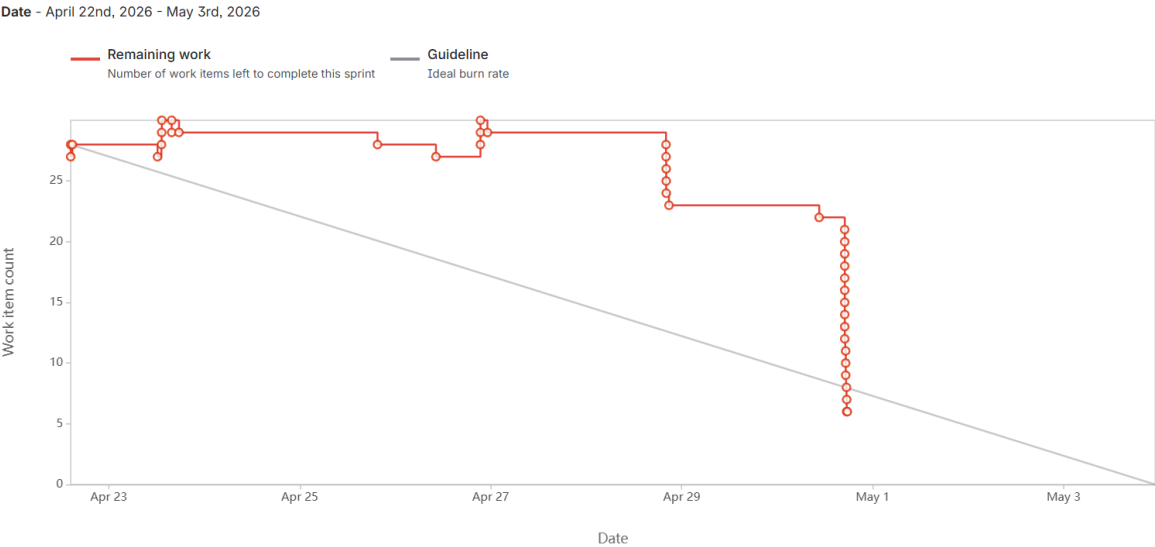


Figure 7: Sprint burndown chart – Work item count

The reason why the report shows that a lot of tickets were moved to DONE in one day is that we have planned a “review meeting” for most of the tasks that we have done during this sprint. Until the final review the tickets remained in the REVIEW category and after our meeting concluded we moved them to DONE.
